



Date of Inspection: 12/8/2020
Facility: Class III Landfill

Annual Inspection Report for CCR Landfills

Reference: 40 CFR Section 257.84, *Inspection Requirements for CCR Landfills*

Owner Information


Name of Landfill: Williams Steam Operations Hwy 52 Class III Ash Landfill
Owner's Name: Dominion Energy South Carolina d.b.a. Dominion Energy
State ID #: #LF3-00001
Owner Contact: Mark Valerio, Environmental Manager
Landfill Location: Goose Creek, SC

Engineer Information

Name and South Carolina License Number: Clark M. Archer, PE 23104
Firm Name: Dominion Energy Environmental Services
Firm Address: 220 Operations Way, MC C221, Cayce, SC 29033-3712
Telephone No.: 803-217-7185

Certification Statement

I certify that the inspection of the above listed CCR landfill was conducted in conformance with the requirements listed in 40 CFR 257.84, and with generally accepted good engineering practices.

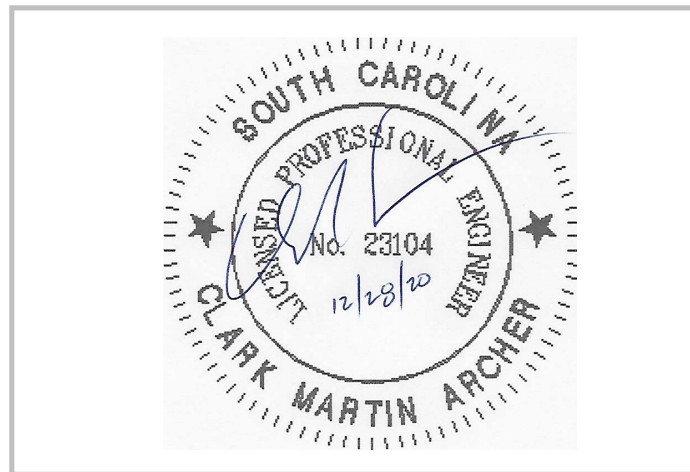

Engineer seal, signature and date

As used herein, the word certify shall mean an expression of the Engineer's professional opinion to the best of his or her information, knowledge and belief, and does not constitute a warranty or guarantee by the Engineer



Date of Inspection: 12/8/2020
Facility: Class III Landfill

Was a review performed of available information regarding the status of the CCR unit, including files in the operating record?

Yes	No
X	

Was a visual inspection performed to identify signs of stress or malfunction of the CCR unit?

X	
---	--

Identify any changes in the geometry of the structure since the previous annual inspection

Fill continues in the active area of the landfill with the objective to reduce the area exposed to precipitation by grading the top surface to slope easterly and then place vegetative cover over the entire top surface except for the active lift area located at the western end. The active lift area will slope westerly to maximize the flow-length of stormwater runoff to the primary drop inlet located at the southeast corner. Except for the east side slope (current active face), vegetative cover is currently placed over all side slopes to minimize erosion and reduce the area exposed to precipitation. Vegetative cover will be placed on the east slope along with the top surface upon completion of grading activities.

Approximate volume of the CCR contained in the unit at the time of inspection

937,000 cubic yards.

Identify any appearances of an actual or potential structural weakness of the CCR unit, in addition to any existing conditions that are disrupting or have the potential to disrupt the operation and safety of the CCR unit

None observed.

Identify any other change(s) which may have affected the stability or operation of the CCR unit since the previous annual inspection.

No other changes observed since previous annual inspection.

Additional comments

None.
